(This SWPPP Template is for the **Common Plan** Permit Only, and

does **NOT** address SWPPP requirements found in the CGP.)

Common Plan SWPPP for

Lot 10 Heart of Pole Patch

4445 N 250 W

Pleasant view Utah 84414

Marquee Homes Inc

P.O Box 208

Roy, Utah 84067

Marquee Homes Inc

3490 W 3300 W West Haven Utah 84401

Date

10-25-2025

1. Project Information

Project Name: Lot 10 Heart of Pole Patch
Address: 4445 N 250 W
City: Pleasant View **State:** UT **Zip:** 84414
Latitude: 41.338794
Longitude:111.980533
UPDES Permit Tracking Number:UTRH10517

Owner: Marquee Homes Inc
Contact Person: Kyle Wayment
Address: P.O Box 208
City: Roy **State:** Utah **Zip:** 84067
Telephone Number: 801-920-4434
Email Address: MarqueeHomesutah@gmail.com

General Contractor: MarqueeHomes Inc
Contact Person: Kyle Wayment
Address: P.O box 208
City: Roy **State:** Utah **Zip:** 84067
Telephone Number: 801-920-4434
Email Address: Marqueehomesutah@gmail.com

Answering "no" to the two questions below means the project is not eligible for this permit.

Is the project in Indian Country? **Yes** ☐ **No** ☒
Is the project a residential building on a single lot and disturbing one acre or less? **Yes** ☒ **No** ☐

2. Pollution Sources/Best Management Practices

Answer yes or no whether the following features are located at your site. If yes, select the BMP(s) that will be used to protect each feature. If no, continue to the next question. Attach necessary illustrated details for proper installation in Appendix G, and show locations of all controls on Site Map in Appendix A.

2.1 **Is there a SWPPP sign on site?** (see permit part 1.10) **Yes** ☒ **Required**
The sign must include the UPDES tracking number, the owner or general contractor name, phone number and email, and if the SWPPP is on-line, instructions on how to view it. The size requirement is to be readable from a publicly accessible point.

2.2 **Will there be construction dewatering on the site?** (see permit part 2.7) **Yes** ☐ **No** ☒
BMP(s): ☐ Dewatering of the construction area is needed and a separate dewatering permit has been obtained to treat and discharge water. *Construction Dewatering (if discharged offsite) must be covered by UPDES Permit UTG070000.*
☐ Water from the dewatering of the construction area will be infiltrated on site.

2.3 **Will there be non-storm water discharges on the site?** (see permit part 1.3) **Yes** ☐ **No** ☒
Allowable discharges include: Flushing of drinking water or irrigation water (not including wash or cleaning waters), water used for dust control, spring water or groundwater not exposed to construction activities, water from emergency fire-fighting activities, and water from foot drains not exposed to construction activities. (see permit part 2.4.5 & 2.9).
Please list all anticipated non-storm water discharges: No anticipated non storm water discharges expected.
What will you do to manage the non-storm water discharges? *Please list direct discharges, contained non-storm water discharges, and discharges that are treated separately.*

BMP(s): ☐ All non-storm water discharges are listed as allowable per permit part 1.3 and discharged
☒ All non-storm water discharges that are not allowed are properly contained (see questions 2.12 and 2.16)
☐ All non-storm water discharges that are contaminated with sediment only (free of chemicals, oils, etc.) will be treated in a sediment basin or equivalent (see permit part 2.8.1).
☐ Other: Click here to enter text.

2.4 **Is it possible for the total area of disturbance to be phased, minimizing the total exposure of disturbed soil at one time?** (see permit part 2.3.1) **Yes ☐** **No ☒**
If disturbance can be minimized please show the locations on the site map and summarize (here) where disturbances will be delayed for some of the disturbed area: Click here to enter text.

2.5 **What perimeter controls will be used to prevent sediment from leaving the site?** (permit part 2.1.2 & 2.3)

BMP(s):
☐ Silt Fence
☐ Vegetative Buffer
☐ Staked straw Wattles (Fiber Rolls)
☒ Berms
☒ Cut-Back-Curb
☐ Weighted Wattles
☐ Other: Click here to enter text.

2.6 **Are surface waters located within 30 feet of your project's earth disturbances?** **Yes ☐** **No ☒**
Note: *A 30' natural vegetative buffer MUST be maintained by water bodies. If a buffer less than 30' is used, you must demonstrate that the additional controls offer the same protection as a 30' natural vegetative buffer, and select the reason for exemption below.* (see permit part 2.3.5)

BMP(s): ☐ 30' Natural Vegetative Buffer
If less than 30' Natural Vegetative Buffer select additional Controls:
☐ 2 Silt Fence Barrier
☐ 2 Straw Wattle Barriers (Fiber Roll)
☐ Other: Click here to enter text.

2.7 **Are there critical or sensitive areas (such as preservation of the drip lines around trees, wetlands, buffer zones by water bodies, etc.) located on or adjacent to the site?** (see permit part 2.2) **Yes ☐** **No ☒**

BMP(s): ☐ Separate and isolate with environmental fencing
☐ Other: Click here to enter text.

2.8 **What track out control will be used to prevent dirt from being tracked on streets as vehicles leave the site?** (see permit part 2.4.1)

BMP(s):
☐ Track Out Pad
☐ Cobble
☒ Gravel
☐ Rumble Strips
☐ Wash Down Pad
☐ Delivery Pad
☐ Restricted Site Access
☐ Selective Access During Dry Weather (Dry soil)
☐ Other: Click here to enter text.

2.9 **Do you have storm drain inlets on or down gradient of this site?** (see permit part 2.1.3) **Yes ☒** **No ☐**
Protection must address the curb inlet opening (throat) as well as the grate.
Where is/are the nearest downstream inlet(s) and how will you protect them: To the south of lot, there will be placed screens and sand bags to protect.

BMP(s):
☒ Rock/Sand-filled Bags
☒ Filter Fabric
☐ Proprietary inlet devices
☐ Other: Click here to enter text.
☐ Drop Inlet Bags
☐ Gravel or Sand filled Wattles

2.10 Will curb ramps be used at the site? (see permit part 2.4.2) **Yes** ☐ **No** ☒

If curb ramps are used it must be done with material [not dirt] that will not wash away in storm water.

BMP(s):
☐ Crushed Rock
☐ Other: Click here to enter text.
☐ Wood/Steel Ramps

2.11 Will there be stockpiles or spoil piles on the site? **Yes** ☐ **No** ☒

Note: *Select "Contained by other BMP" if another BMP on your site will contain runoff from the stockpiles. Materials that can be transported with precipitation must not be placed in the street.* (see permit part 2.1.1)

BMP(s):
☐ Surrounded by Silt Fence
☐ Covered with Tarp
☐ Surrounded by Staked Straw Wattles
☐ Temporary – Removed same day
☐ Contained by other BMP. Explain: Click here to enter text.
☐ Other: Click here to enter text.

2.12 Does the project include installation of concrete, masonry, stucco, and paint (water based)work in this project? (see permit part 2.4.5 & 2.9.1) **Yes** ☒ **No** ☐

Wash water must be contained, the solids dried, and disposed of at a landfill.

BMP(s):
☒ Lined Depression
☐ Regional Washout (per development)
☒ Other: Wash out pool
☐ Steel Dumpster

2.13 How will solid waste be dealt with on the site? (see permit part 2.4.3)

Light trash in uncovered dumpsters can blow out and scatter with wind and rain may fall on uncovered leachable material in the dumpster and leak out the bottom causing pollutants to escape.

BMP(s):
☐ Bag Lightweight Trash
☐ Receptacles with Lids
☒ Leak Proof Dumpsters
☐ Other: Click here to enter text.

2.14 Will there be a need to dispose of solvents, oil, fuel, etc. liquid waste? (see permit part 2.9) **Yes** ☐ **No** ☒

BMP(s):
☐ Contained and Removed from the site
☐ Other: Click here to enter text.
☐ Collected for Reuse

2.15 How will sanitary waste be handled on the site? (see permit part 2.4.4)

BMP(s):
☒ Portable Toilet(s) *(must be staked down on dirt surface & 10' from curb)*
☐ Onsite or Adjacent Indoor Bathrooms
☐ Portable Toilet Secondary Containment (secured down with straps to heavy weights)
☐ Other: Click here to enter text.

2.16 How will you minimize the discharge of pollutants from spills and leaks? (see permit part 2.8.3)

BMP(s):
☐ Use of drip pans
☐ Spill kit
☐ Other: Click here to enter text.
☒ Offsite fueling, and maintenance
☐ Spill response plan.

2.17 Will there be a need to store construction materials on site? (see permit 2.8.2) **Yes** ☒ **No** ☐

Minimize the exposure of materials with a pollution risk (certain building and landscaping materials, fertilizers, pesticides, herbicides, detergents).

BMP(s): ☐ Covering Erodible or Liquid Materials ☐ Secondary Containment
☒ Strategic Storage and Staging ☐ Stored off-site
☐ Enclose them in a weather proof shed.
☒ Other: Materials will be stored in the front area of the lot in the track in track out area, and will be left in their shipping pachaging until use to minimize any exposure.

2.18 Does your site have steep slopes (greater than 70%)? (see permit part 2.3.2) **Yes** ☐ **No** ☒

BMP(s): ☐ Erosion Control Blanket ☐ Avoid Disturbance on slope
☐ Seeding ☐ Hydroseed
☐ Mulch ☐ Takifiers
☐ Other: Click here to enter text.

2.19 Are there site conditions that cause storm water flows with highly erosive velocities? (see permit parts 2.3.3 and 2.3.4) **Yes** ☐ **No** ☒

Flows must be controlled to minimize sediment transport.

BMP(s): ☐ Gravel Check Dam ☐ Straw Wattles (Fiber Rolls) Check Dam
☐ Divert Flows around the Site ☐ Armored channel (riprap, geotextile, other)
☐ Other: Click here to enter text.

2.20 How will you reduce storm water volume to minimize sediment transport, channel and stream bank erosion? (see permit parts 2.3.4 and 2.3.3)

BMP(s): ☐ Utilize basin, depression storage of storm water, cut back curb, or other to hold and infiltrate.
☐ Prevent heavy equipment (as much as possible) from compacting soil so storm water will infiltrate easier.
☒ Rip soil after heavy equipment has caused compaction.
☐ Other: Click here to enter text.

2.21 Is there a need for dust control on the site (regulatory or for practical reasons)? **Yes** ☐ **No** ☒

BMP(s): ☐ Wetting with Water ☐ Cover dirt piles with a tarp
☐ Use Magchloride, Calcium Chloride or Lignan Sulfonate
☐ Stabilize surface with mulch, gravel or other surface cover
☐ Other: Click here to enter text.

2.22 Will there be disturbed areas on the site that will need to be temporarily stabilized before the project is completed? (see permit part 2.6) **Yes** ☐ **No** ☒

Places that are disturbed and then left for over 14 days with no activity, must be temporarily or permanently stabilized.

BMP(s): ☐ Bark or other mulch ☐ Hydro-mulch ☐ Seeding
☐ Tackifier ☐ Staked netting with straw mulch
☐ Other: Click here to enter text.

2.23 Will the house be sold without any landscaping? **Yes** ☒ **No** ☐

If so, how will you leave the site for the new home owner so sediment will be contained on site until the home owner completes landscaping? *(the permit can be terminated when the owner occupies the house even though the site is not stabilized).*

BMP(s): ☐ Mulching/Hydro-mulching ☐ Swales ☐ Silt Fence

☐ Wattles ☒ Cut-Back-Curb ☐ Seeding
☐ Vegetated Buffer ☒ Grade Front-Yard Lower than Sidewalk
☐ Other: Click here to enter text.

3. Sequence of Construction Activity

Type of Construction Activity	Approximate Date Range
Start/End of the Project	11-17-2025
Excavation activities	11-18-2025
Foundation/Footings	11-25-2025
Backfill	11-30-2025
Erection of Building	11-30-2025
Utility Lines installed (you may need to separate this into Plumbing lines, electrical lines, gas lines, water lines, Internet lines, etc.)	11-30-2025
Insert more rows for any stage that should be included	
Landscaping (if the house is sold or occupied by owner with landscaping, if not landscaping should not be included)	

4. Site Map

On a blank page (or include a page from the architectural drawings that show site layout and dimensions), please draw a map (and place this map in Appendix A) showing the layout of the site including locations of:

1. boundaries of project/property
2. boundaries of disturbance (including areas outside of property boundaries)
3. show slopes on site (if there are steep areas show steep areas)
4. location of structures/facilities
5. locations of :
    a. stockpiles for soils and materials
    b. construction supplies
    c. portable toilets
    d. garbage/trash containers
    e. egress points/track out pads
    f. concrete washout pits or containers
6. water bodies, wetlands, natural vegetative buffers

7. placement of all BMPs, perimeter, erosion control, sediment control, inlet protection, etc.
8. storm water inlets and storm water discharge points (where storm water drains off the site)
9. areas that will be temporarily or permanently stabilized on the site
10. areas where disturbances will be delayed to minimize total exposed surface at one time.

5. Potential Sources of Pollutants

Potential sources of sediment to storm water runoff:

- Clearing and grubbing operations
- Grading and site excavation operations
- Vehicle tracking
- Topsoil stripping and stockpiling
- Landscaping operations

Potential pollutants and sources, other than sediment, to storm water runoff:

- Combined Staging Area—small fueling activities, minor equipment maintenance, sanitary facilities, and hazardous waste storage.
- Materials Storage Area—general building materials, solvents, adhesives, paving materials, paints, aggregates, trash, and so on.
- Construction Activity—paving, curb/gutter installation, concrete pouring/mortar/stucco, and building construction
- Concrete Washout Area

For all potential construction site pollutants, see Table 2 below.

Table 2. Potential construction site pollutants. Circle all that applies to your site and in the last column identify pollution prevention measures to minimize their discharge.

Material/Chemical	Storm Water Pollutants	Common Location*	Pollution Prevention Methods
Pesticides (insecticides, fungicides, herbicides, rodenticide)	Chlorinated hydrocarbons, organophosphates, carbamates, arsenic	Herbicides used for noxious weed control	None will be stored on site.
Fertilizer	Nitrogen, phosphorous	Newly seeded areas	None will be stored on site.
Plaster	Calcium sulphate, calcium carbonate, sulfuric acid	Building construction	Washout basin.
Cleaning solvents	Perchloroethylene, methylene chloride, trichloroethylene, petroleum distillates	No equipment cleaning allowed in project limits	Washout Basin.
Asphalt	Oil, petroleum distillates	Streets and roofing	N/A
Concrete	Limestone, sand, pH, chromium	Curb and gutter, building construction	Washout Basin.

Material/Chemical	Storm Water Pollutants	Common Location*	Pollution Prevention Methods
Glue, adhesives	Polymers, epoxies	Building construction	Washout Basin.
Paints	Metal oxides, Stoddard solvent, talc, calcium carbonate, arsenic	Building construction	Washout Basin.
Curing compounds	Naphtha	Curb and gutter	N/A
Wood preservatives	Stoddard solvent, petroleum distillates, arsenic, copper, chromium	Timber pads and building construction	None will be stored on site.
Hydraulic oil/fluids	Mineral oil	Leaks or broken hoses from equipment	None will Be stored on site.
Gasoline	Benzene, ethyl benzene, toluene, xylene, MTBE	Secondary containment/staging area	None will be stored on site.
Diesel Fuel	Petroleum distillate, oil & grease, naphthalene, xylenes	Secondary containment/staging area	None will be stored on site.
Kerosene	Coal oil, petroleum distillates	Secondary containment/staging area	None will be stored on site.
Antifreeze/coolant	Ethylene glycol, propylene glycol, heavy metals (copper, lead, zinc)	Leaks or broken hoses from equipment	None will be stored on site.
Sanitary toilets	Bacteria, parasites, and viruses	Staging area	Porta John, company spill guide.

*(Area where material/chemical is used on-site)

6. Spill Prevention and Response Plan

Describe the spill prevention and control plan to include ways to reduce the chance of spills, stop the source of spills, contain and cleanup spills, dispose of materials contaminated by spills, and train personnel responsible for spill prevention and control. Additionally, fill in all **BLUE** fields below.

Spill Plan:

Will mitigate spills promptly and depending on spill manage accordingly.

Any discharges in 24 hours equal to or in excess of the reportable quantities listed in 40 CFR 117, 40 CFR 110, and 40 CFR 302 will be reported to the National Response Center and the Division of Water Quality

(DWQ) as soon as practical after knowledge of the spill is known to the permittee. The permittee shall submit within 14 calendar days of knowledge of the release a written description of: the release (including the type and estimate of the amount of material released), the date that such release occurred, the circumstances leading to the release, and measures taken and/or planned to be taken to the Division of Water Quality (DWQ), 288 North 1460 West, P.O. Box 144870, Salt Lake City, Utah 84114-4870. The Storm Water Pollution Prevention Plan must be modified within14 calendar days of knowledge of the release to provide a description of the release, the circumstances leading to the release, and the date of the release. In addition, the plan must be reviewed to identify measures to prevent the reoccurrence of such releases and to respond to such releases, and the plan must be modified where appropriate.

Agency	Phone Number
National Response Center	(800) 424-8802
Division of Water Quality (DWQ) 24-Hr Reporting	(801) 538-6146; (801) 536-4123
Utah Department of Health Emergency Response	(801) 580-6681
Local Fire Department	911

Minimum spill quantities requiring reporting:

Material	Media Released To	Reportable Quantity
Engine oil, fuel, hydraulic & brake fluid	Land	25 gallons
Paints, solvents, thinners	Land	100 lbs (13 gallons)
Engine oil, fuel, hydraulic & brake fluid	Water	Visible Sheen
Refrigerant	Air	1 lb
Antifreeze, battery acid, gasoline, engine degreasers	Air, Land, Water	100 lbs (13 gallons)

Emphasis to:

1st Priority: Protect all people (including onsite staff)
2nd Priority: Protect equipment and property
3rd Priority: Protect the environment

1. Make sure the spill area is safe to enter and that it does not pose an immediate threat to health or safety of any person.
2. Check for hazards (flammable material, noxious fumes, cause of spill) – if flammable liquid, turn off engines and nearby electrical equipment. If serious hazards are present leave area and call 911. LARGE SPILLS ARE LIKELY TO PRESENT A HAZARD.
3. Stop the spill source and contain flowing spills immediately with spill kits, dirt or other material that will achieve containment.
4. Call co-workers and supervisor for assistance and to make them aware of the spill and potential dangers
5. If spilled material has entered a storm sewer, regardless of containment; contact the City Storm Water Division.
6. Cleanup all spills (flowing or non-flowing) immediately following containment. Clean up spilled material according to manufacturer specifications, for liquid spills use absorbent materials AND DO NOT FLUSH AREA WITH WATER.

7. Properly dispose of cleaning materials and used absorbent material according to manufacturer specifications.
8. Report the reportable quantity to the Pleasant View City Storm Water Division.

Emergency Numbers

Utah Hazmat Response Officer 24 hrs	(801)-538-3745
City Police Department	911
City Engineering Division	801-782-8529

7. SWPPP, Inspections and Corrective Action Reports

Inspection Schedule and Procedures: The permit requires inspections once a week (see permit Part 3). You must list and provide details of your BMPs in Appendix G. Inspection reports require reporting on BMPs and how effective they are (download inspection reports from the DWQ construction storm water website under the Common Plan Permit). You may be required to maintain, modify, remove, or apply/install more or different BMPs to control pollutants on the site. Please number your BMPs in Appendix G and refer to those numbers on your inspection reports and corrective action reports when you inspect or report on them.

Describe the general procedures for correcting problems when they are identified. Include responsible staff and time frames for making corrections:

Problems that are discovered will be corrected promptly and based according to the problem.

Inspections and Corrective Actions: All inspections and corrective actions must be logged using the "Inspection/Correction Action Log" attached in Appendix E. The log should be filled out completely for each BMP.

8. Training of Sub-Contractors

All sub-contractors, installers of utility connections, and others that perform activities that are affected by permit requirements will be informed about permit requirements that pertain to their scope of work.

Sub-Contractors that have been informed:

Contractor	Date	Topic(s) Covered	Initials of Trainer
Excavator			
Gas utilities			
Plumbing connection			
Electrical connection			

Concrete foundation walls			
Concrete flat work			
Landscaper			
Other: Click here to enter text.			
Other: Click here to enter text.			
Other: Click here to enter text.			
Other: Click here to enter text.			

9. Changes to the SWPPP

All changes to this SWPPP must be redlined, dated, and initialed in the SWPPP document and on the site map.

10. Record Keeping

The following items should be kept at the project site available for inspectors to review:

1. A copy of the Common Plan Permit (Appendix B)
2. The signed and certified NOI form (Appendix C)
3. Inspection reports (Appendix E)

11. Delegation of Authority (if any)

Duly Authorized Representatives or Positions:

Company/Organization: Company of Representative.
Name: Authorized Representative Name.
Position: Representative Title.
Address: Click here to enter text.
City: Click here to enter text. State: State Zip: Zip Code
Telephone: (XXX) XXX-XXXX Fax/Email: (XXX) XXX-XXXX

Owner/General Contractor Signature:_____ Date:_____

No Delegation of Authority

Additional Duly Authorized Representatives or Positions:

Company/Organization: Company of Representative.
Name: Authorized Representative Name.
Position: Representative Title.
Address: Click here to enter text.
City: Click here to enter text. State: State Zip: Zip Code
Telephone: (XXX) XXX-XXXX Fax/Email: (XXX) XXX-XXXX

Owner/General Contractor Signature:_____ Date:_____

No Delegation of Authority

12. Discharge Information

Does your project/site discharge storm water into a Municipal Separate Storm Sewer System (MS4)?

☒ Yes ☐ No

Municipal Storm Drain System receiving the discharge from the construction project: Pleasant View City

Receiving Waters (look up https://deq.utah.gov/ProgramsServices/programs/water/standards/WQmap.htm to identify your receiving water body)

Enter the name(s) of the first surface water(s) that receives storm water directly from your site and/or from the MS4 listed above. **Note:** *multiple rows provided in the case that your site has more than one point of discharge in which each flows to different surface waters.*

1. **Howard Slue**
2. Click here to enter name of receiving waters.
3. Click here to enter name of receiving waters.
4. Click here to enter name of receiving waters.

Impaired Waters (refer to http://mapserv.utah.gov/surfacewaterquality/ in the left hand column to determine status of receiving water body).

Select any impaired surface water(s) that your site will discharge to, either directly or through the MS4 selected above.

Impaired Surface Water	Is this surface water impaired?	Pollutant(s) causing the impairment	Has a TMDL been completed?	Pollutant(s) for which there is a TMDL
Click here to enter text.	☐ Yes ☐ No	Click here to enter text.	☐ Yes ☐ No	Click here to enter text.
Click here to enter text.	☐ Yes ☐ No	Click here to enter text.	☐ Yes ☐ No	Click here to enter text.

13. Certification and Notification

I, Kyle C Wayment , certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

X

Construction Operator:

This SWPPP should be signed and certified by the construction operator(s).

SWPPP Appendices

Ensure the following documentation is attached to the SWPPP:

Appendix A: SWPPP Site Maps

Appendix B: Common Plan Permit

Appendix C: Notice of Intent (NOI), and a copy of the NOT form unless you plan to terminate the permit on-line

Appendix D: Daily Site Check Log

Appendix E: Inspection Reports and Corrective Actions

Appendix F: Additional Information (i.e. permits such as local permits, dewatering, stream alteration, wetland, and out of date SWPPP documents, delegation of authority forms, etc.)

Appendix G: BMP Specifications and Details (label BMPs to match the sections identified in this document.)

APPENDIX A: SWPPP Site Maps

NOTE

LOT SHALL BE GRADED TO DRAIN SURFACE WATER AWAY FROM CONCRETE WALLS. THE GRADE AWAY FROM THE FOUNDATION SHALL FALL A MINIMUM OF 6" WITHIN THE FIRST 10 FEET. (5%)

NOTE

DUST, MUD, AND EROSION SHALL BE CONTROLLED BY WHATEVER MEANS NECESSARY, AND THE ROADWAY SHALL BE KEPT FREE OF MUD AND DEBRIS AT ALL TIMES.

BUILDER-OWNER SHALL REPLACE ANY CURB OR GUTTER ALONG THE FRONTAGE OF THIS PROJECT, THAT IS FOUND TO BE DEFECTIVE, AS DIRECTED BY CITY INSPECTOR.

A PROFESSIONAL ENGINEER, CURRENTLY LICENSED IN UTAH, SHALL INSPECT AND APPROVE ANY RETAINING WALLS THAT ARE HIGHER THAN 4', ONCE CONSTRUCTED.

NOTE

•ALL STORM WATER AND DIRT WILL BE KEPT ON SITE DURING CONSTRUCTION UNTIL FINAL LANDSCAPING IS DONE.

•GENERAL CONTRACTOR WILL BE HELD RESPONSIBLE FOR DIRT/MUD ON SITE DURING BAD WEATHER AND FOR CLEANING UP AFTER SUBCONTRACTORS.

•STREET, CURB AND GUTTER WILL BE INSPECTED AND CLEANED OF ALL MUD AND DIRT AT THE END OF EVERY DAY.

•GRAVEL BAGS TO BE PLACED AND MAINTAINED AROUND ANY STORM DRAIN INLET ADJACENT TO OR IMMEDIATELY DOWNSTREAM FROM SITE DURING CONSTRUCTION.

•BERMS AND SWALES MAY BE REQUIRED ALONG PROPERTY LINES TO PREVENT STORM WATER FLOW ONTO ADJACENT LOTS. FINAL GRADING TO BLEND WITH ADJACENT LOTS.

•DRAINAGE ALONG REAR DRAINAGE EASEMENT MUST BE MAINTAINED AFTER LANDSCAPING TO ALLOW FLOW FROM SURROUNDING LOTS TO CROSS THE LOT AS SHOWN ON SUBDIVISION GRADING PLAN.

•A LINED CONCRETE WASHOUT AREA MUST BE PROVIDED AT THE SITE FOR ALL CONCRETE WORK. WASHOUT INTO THE FOUNDATION OR ON THE GROUND IS PROHIBITED.

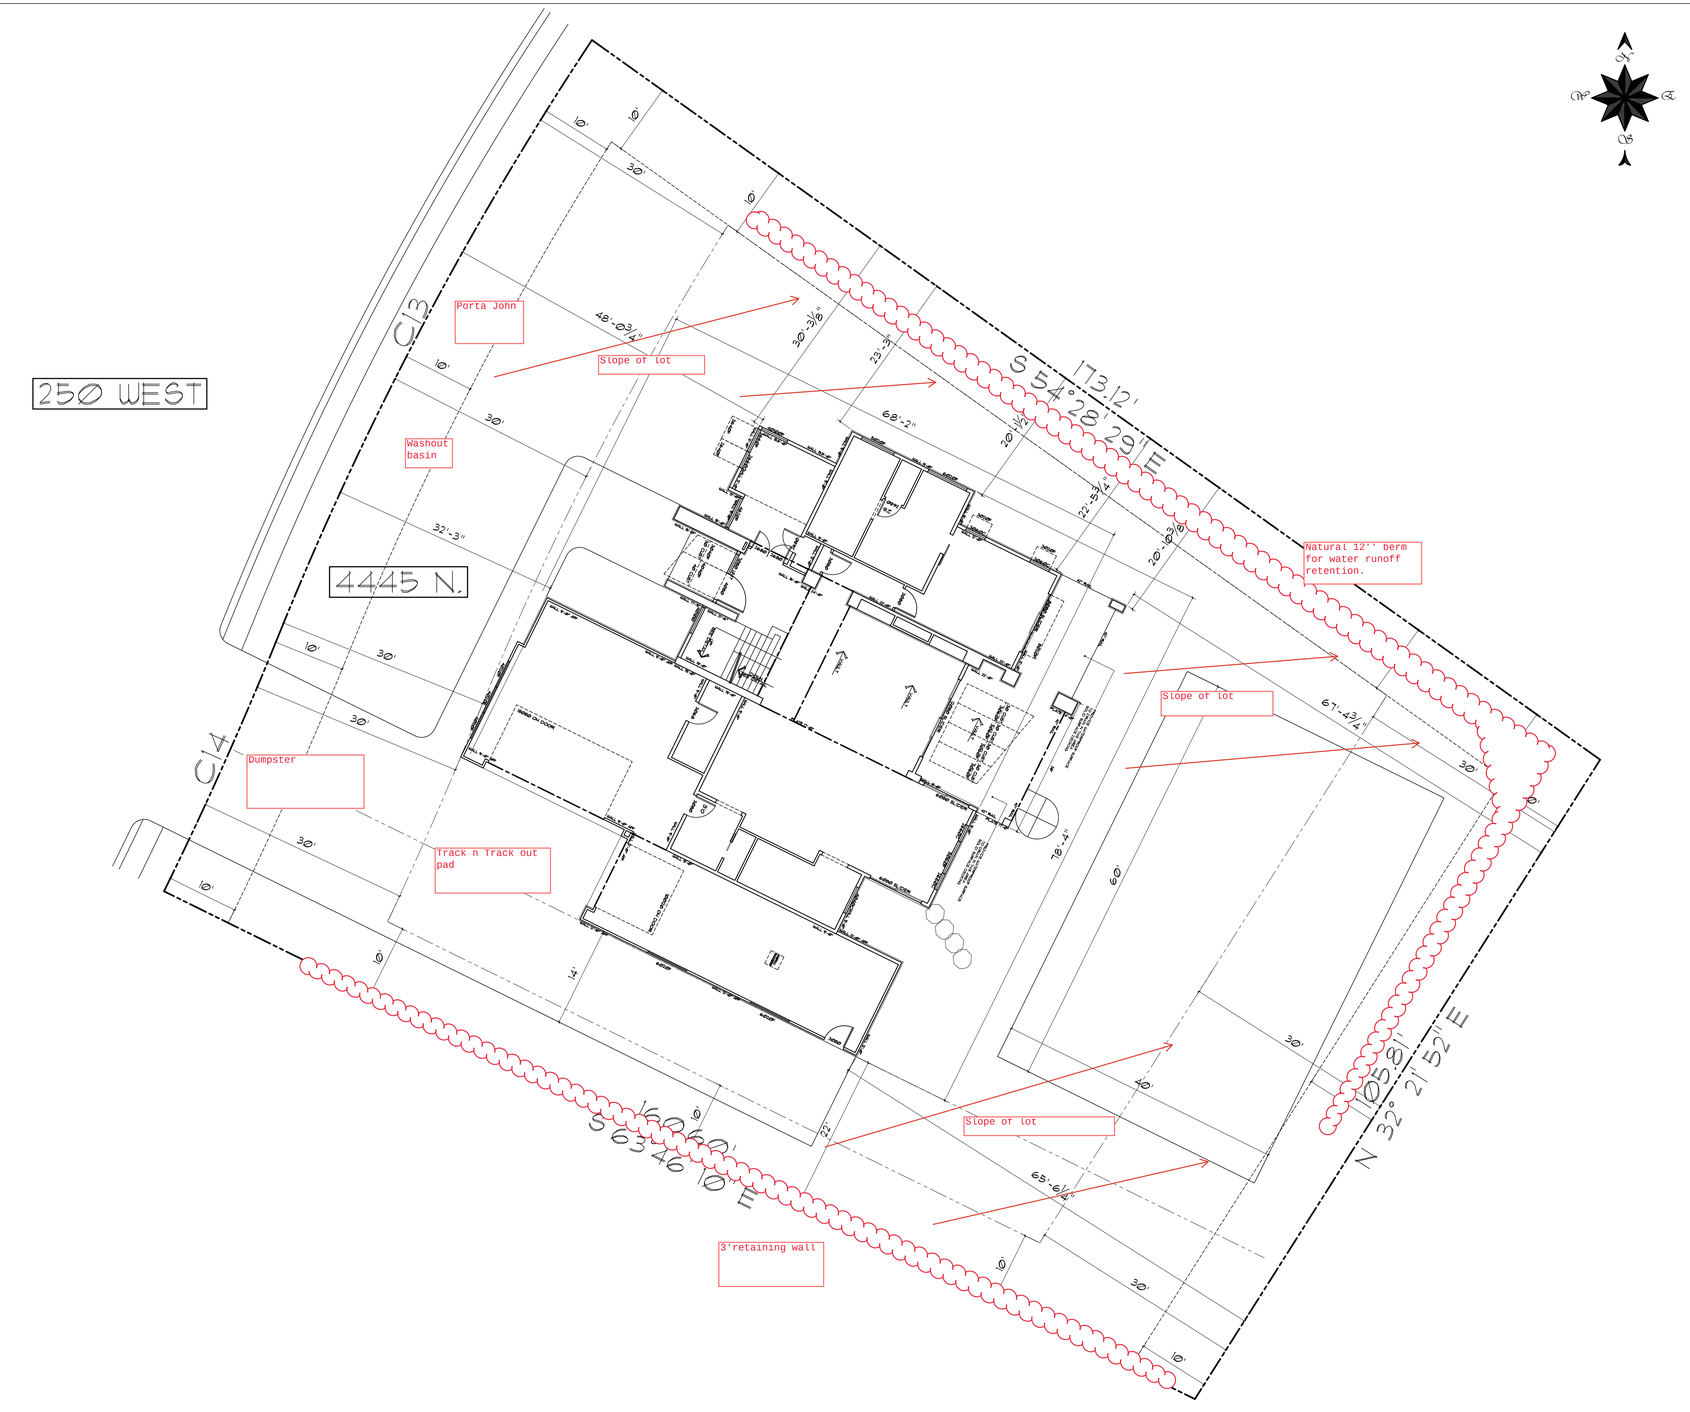

A SITE PLAN

SCALE: 1" = 10'

rml DESIGN

420 E. SOUTH TEMPLE
SUITE 515
SALT LAKE CITY, UTAH 84111
801. 217. 3727

ATTENTION

RML DESIGN MAINTAINS THE INTELLECTUAL RIGHTS TO THIS PROPERTY. ALL RIGHTS ARE RESERVED, AND SHALL NOT BE REPRODUCED OR COPIED WITHOUT THE EXPRESSED WRITTEN CONSENT OF RML DESIGN, UNDER PENALTY OF PROSECUTION.

THESE PLANS MAY NOT BE USED FOR THE CONSTRUCTION OF ANY BUILDING EXCEPT THE ONE FOR WHICH THESE PLANS WERE ORIGINALLY ISSUED. SUCH USE WILL INDICATE AN UNAUTHORIZED USE OF COPYRIGHTED MATERIAL

© ALL RIGHTS RESERVED

PROJECT NAME:
LOT 2 HEART OF POLE PATCH

LOCATION INFO:
LOT #
10
SUBDIVISION
HEART OF POLE PATCH
CITY
PLEASANT VIEW
STATE
UTAH

CLIENT NAME:
MARQUEE HOMES

PLAN NAME:
CUSTOM

ORIGINAL RELEASE:
OCTOBER 10, 2025

REVISION DATES
XX/XX/XXXX
XX/XX/XXXX
XX/XX/XXXX
XX/XX/XXXX

MARQUEE25T1-C-MARQ-10-23-C

SITE PLAN

A1 | 1

APPENDIX B: Common Plan Permit

Find the permit on https://deq.utah.gov/Permits/water/updes/stormwatercon.htm

APPENDIX C: Notice of Intent and Termination.

Find the Notice of Termination Form at
https://deq.utah.gov/Permits/water/updes/stormwatercon.htm

However, termination of the project can be done on-line at https://secure.utah.gov/stormwater

(You must log in using the same username that you applied for your NOI with. If you completed a paper NOI you must complete a paper NOT.)

APPENDIX D: Daily Self-Inspection Log (permit part 3.2.2).

Daily Inspection Log

Date	Initials	Date	Initials	Date	Initials	Date	Initials

APPENDIX E: Inspection Reports

Include BMPs inspected even if they are in good condition. Corrections must be completed before the next weekly inspection.

Weekly Inspection/Corrective Action Log							
Date & Time of Inspection	**Weather**	**BMP # and Name**	**Description of BMP Condition or Deficiency**	**Initial**	**Correction Date (MM/DD/YY)**	**How the BMP was Corrected**	**SWPPP Changed (Y/N)**

APPENDIX F: Additional Information

For permits such as local permits, dewatering, stream alteration, wetland, and out of date SWPPP documents, delegation of authority forms, etc.

Delegation of Authority

I, _____ (name), hereby designate the person or specifically described position below to be a duly authorized representative for the purpose of overseeing compliance with environmental requirements, including the Common Plan Permit, at the _____ construction site. The designee is authorized to sign any reports, stormwater pollution prevention plans and all other documents required by the permit.

_____ (name of person or position)

_____ (company)

_____ (address)

_____ (city, state, zip)

_____ (phone)

By signing this authorization, I confirm that I meet the requirements to make such a designation as set forth in _____ (Reference State Permit), and that the designee above meets the definition of a "duly authorized representative" as set forth in _____ (Reference State Permit).

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Name:

Company:

Title:

Signature:

Date:

APPENDIX G: BMP Specifications and Details

Label BMPs to match the sections identified in this document.

Below are links to various Construction Storm Water BMP Manuals for reference.

Salt Lake County
http://slco.org/uploadedFiles/depot/publicWorks/engineering/final_bmp_constructi.pdf
BEST MANAGEMENT PRACTICES FOR CONSTRUCTION ACTIVITIES

Davis County
http://www.daviscountyutah.gov/docs/librariesprovider20/default-document-library/stormwater-best-management-practices.pdf?sfvrsn=c9cd4053_2
A Guide to Stormwater Best Management Practices

Nevada DOT
https://www.nevadadot.com/home/showdocument?id=9417
Stormwater Quality Manuals: Construction Site Best Management Practices (BMPs) Manual

Caltrans
http://www.dot.ca.gov/hq/construc/stormwater/CSBMP-May-2017-Final.pdf
Construction Site Best Management Practices (BMP) Manual

Oregon
http://www.oregon.gov/deq/FilterPermitsDocs/BMPManual.pdf
Construction Stormwater Best Management Practices Manual

Los Angeles
http://dpw.lacounty.gov/cons/specs/BMPManual.pdf
Construction Site Best Management Practices (BMPs) Manual

Maricopa County (Arizona)
https://www.maricopa.gov/DocumentCenter/View/2368/2015-03-Drainage-Design-Manual-for-Maricopa-County-Volume-III-Erosion-pdf
Drainage Design Manual for Maricopa County (Erosion Control)

Minnesota
https://www.pca.state.mn.us/sites/default/files/wq-strm2-09.pdf
Stormwater Compliance Assistance Toolkit for Small Construction Operators
